SEMMMS A6MARR PROGRAMME
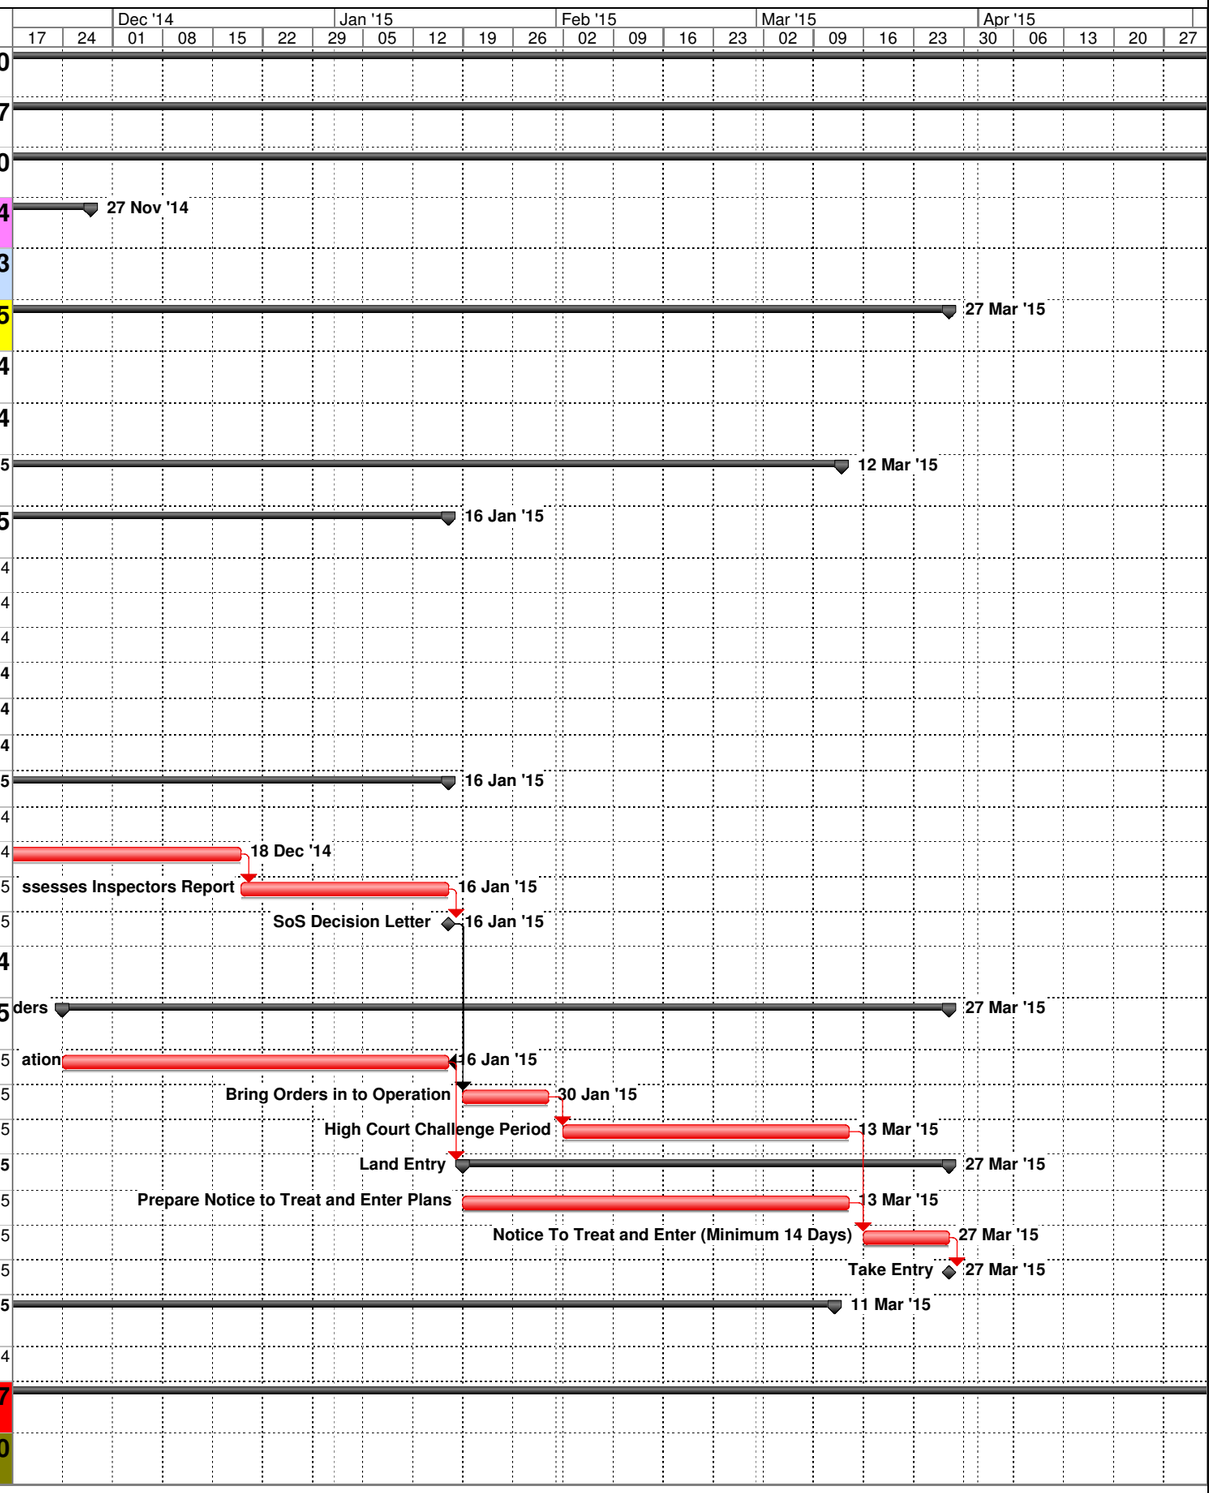
ID	WBS	Task Name	Duration	Start	Finish
1	1	**A6 to Manchester Airport Relief Road**	**499.2 wks**	**Fri 18/02/11**	**Mon 16/11/20**
2	1.1	**Key Project Milestones**	**260.8 wks**	**Fri 07/09/12**	**Mon 23/10/17**
12	1.2	**Project Management**	**499.2 wks**	**Fri 18/02/11**	**Mon 16/11/20**
21	1.3	**Stage 2 Options Selection and Planning Ap**	**191.2 wks**	**Mon 21/02/11**	**Thu 27/11/14**
343	1.4	**Publish Draft Orders and Procure ECI Con**	**63.6 wks**	**Fri 14/09/12**	**Thu 12/12/13**
425	1.5	**Key Stage 4 Statutory Procedures and Pow**	**73 wks**	**Fri 18/10/13**	**Fri 27/03/15**
426	1.5.1	**KS3 Design Development**	**40 wks**	**Wed 30/10/13**	**Thu 14/08/14**
431	1.5.2	**Traffic Modelling - Oct 13 to Sept 14**	**45.8 wks**	**Fri 18/10/13**	**Mon 15/09/14**
465	1.5.3	**Pre-Construction Surveys**	**48 wks**	**Tue 01/04/14**	**Thu 12/03/15**
504	1.5.4	**KS4 Public Inquiry Stage**	**55 wks**	**Fri 13/12/13**	**Fri 16/01/15**
505	1.5.4.1	Objection Period	6.6 wks	Fri 13/12/13	Fri 31/01/14
506	1.5.4.2	Minister Consider Objections	3 wks	Mon 03/02/14	Fri 21/02/14
507	1.5.4.3	Announce Intention to Hold Inquiry (Relevant Date)	0 wks	Fri 21/02/14	Fri 21/02/14
508	1.5.4.4	**April 2014 Additional CPO Notices**	**8.2 wks**	**Wed 30/04/14**	**Mon 30/06/14**
522	1.5.4.5	**Counsel Conferences**	**25 wks**	**Tue 18/03/14**	**Mon 15/09/14**
530	1.5.4.6	**Prepare for Public Inquiry**	**30 wks**	**Mon 24/02/14**	**Fri 26/09/14**
546	1.5.4.7	**Public Inquiry**	**15.2 wks**	**Tue 30/09/14**	**Fri 16/01/15**
547	1.5.4.7.1	Hold Inquiry	2.8 wks	Tue 30/09/14	Fri 17/10/14
548	1.5.4.7.2	Inspectors Report	8.8 wks	Mon 20/10/14	Thu 18/12/14
549	1.5.4.7.3	DfT Considers/Assesses Inspectors Report	3.6 wks	Fri 19/12/14	Fri 16/01/15
550	1.5.4.7.4	SoS Decision Letter	0 wks	Fri 16/01/15	Fri 16/01/15
551	1.5.5	**ECI Contractor Support**	**10 wks**	**Fri 01/08/14**	**Fri 10/10/14**
555	1.5.6	**Confirm Orders**	**17.4 wks**	**Mon 24/11/14**	**Fri 27/03/15**
556	1.5.6.1	Prepare & Issue CPO Notices of Confirmation	7.4 wks	Mon 24/11/14	Fri 16/01/15
557	1.5.6.2	Bring Orders in to Operation	2 wks	Mon 19/01/15	Fri 30/01/15
558	1.5.6.3	High Court Challenge Period	6 wks	Mon 02/02/15	Fri 13/03/15
559	1.5.6.4	**Land Entry**	**10 wks**	**Mon 19/01/15**	**Fri 27/03/15**
560	1.5.6.4.1	Prepare Notice to Treat and Enter Plans	8 wks	Mon 19/01/15	Fri 13/03/15
561	1.5.6.4.2	Notice To Treat and Enter (Minimum 14 Days)	2 wks	Mon 16/03/15	Fri 27/03/15
562	1.5.6.4.3	Take Entry	0 wks	Fri 27/03/15	Fri 27/03/15
563	1.5.7	**Final MSBC Approval**	**27 wks**	**Mon 01/09/14**	**Wed 11/03/15**
568	1.5.8	Client issues instruction to proceed to KS6	0 wks	Fri 29/08/14	Fri 29/08/14
569	1.6	**KS6 ECI Contractor**	**156.6 wks**	**Mon 29/09/14**	**Mon 23/10/17**
683	1.7	**Stage 7 Handover and Close Out**	**160 wks**	**Tue 24/10/17**	**Mon 16/11/20**
